

APPR

WEXEC

APPR

WEXEC

APPR

APPR

INPRG

INPRG

INPRG

INPRG

COMP

INPRG

INPRG

COMP

COMP

INPRG

INPRG

COMP

COMP

Agile EMS Operations Playbook

Mastering Work Management: Preventive
Maintenance & Daily Inspection Cycles


For Service Engineers, Operations, and CHE Engineers.

Core Workflows:

Defining the Maintenance Ecosystem

	Preventive Maintenance (PM)	Daily Inspection (DI)
Core Purpose	Systematic inspection and correction of incipient failures.	Routine check of asset/location readiness for operation.
Schedule & Trigger	Time-to-time planned guidelines.	Daily (before/after operation).
Downtime Requirement	Always requires downtime (must minimize business impact).	No structural downtime required.
Initial System Status	APPR (Approved)	WEXEC (Waiting to Execute)

The Lifecycle of a Preventive Maintenance (PM) Work Order

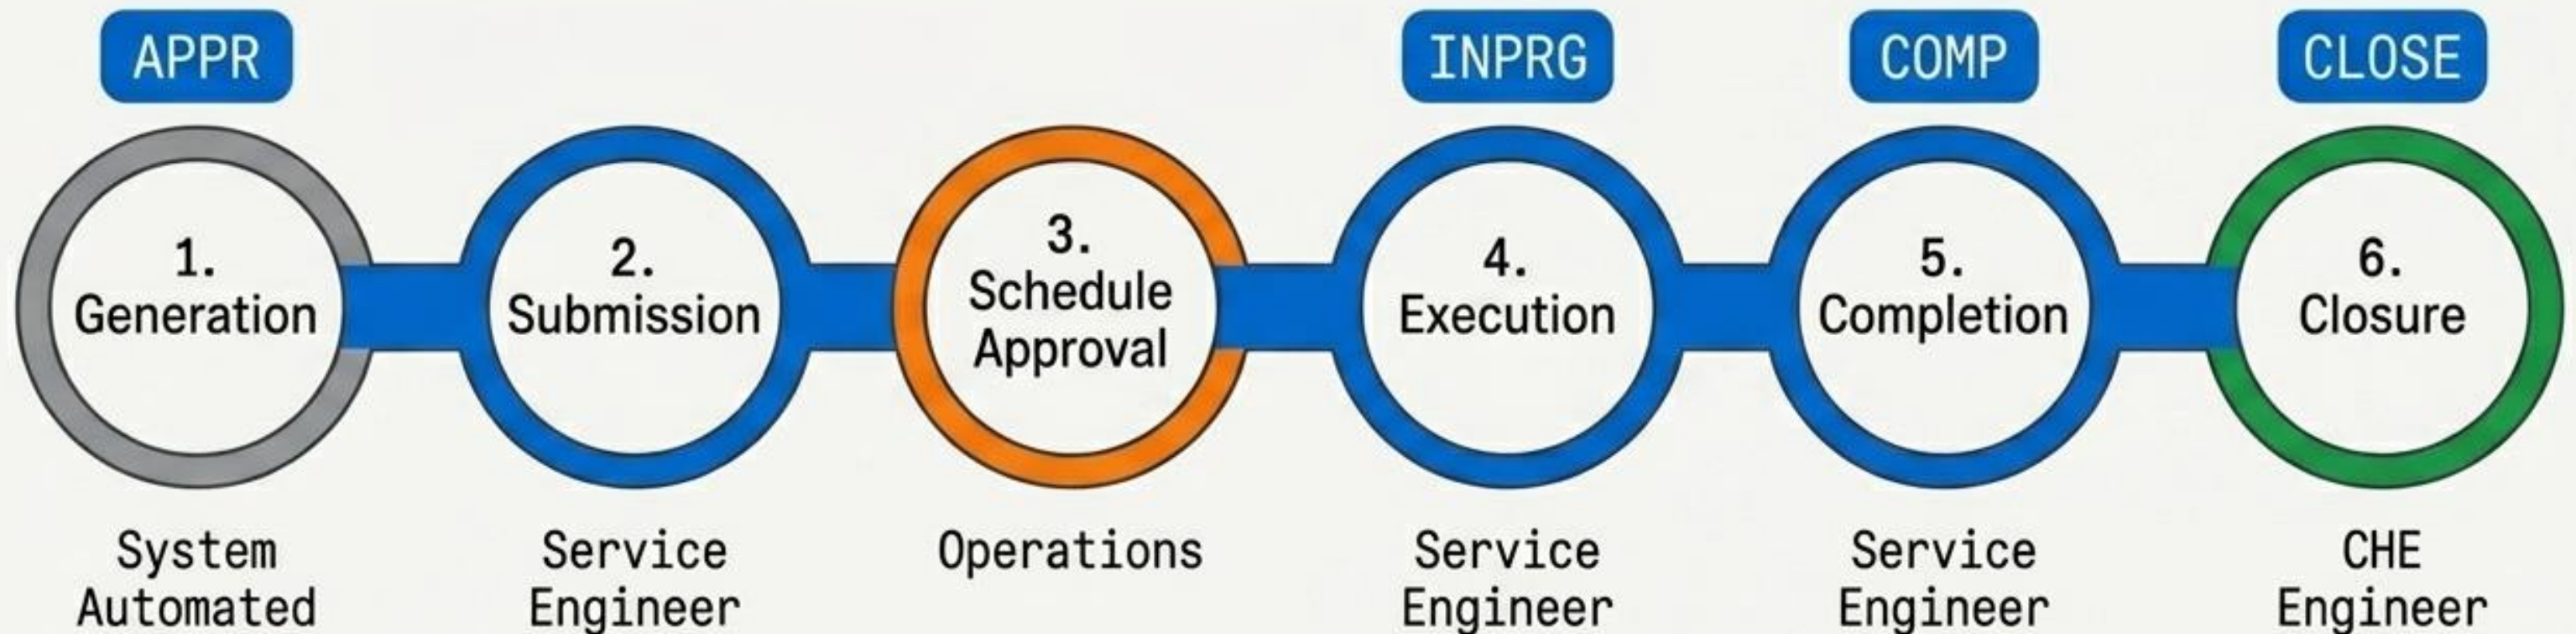

System
Automated



Service
Engineer



Operations



CHE Engineer

Step 1: Scheduling and Initiating the PM Workflow



Action Checklist (Service Engineer)

1. Open Assignment in Start Center.
2. Input Target Scheduled Start and Scheduled Finish.
3. Crucial: Check the 'Requires Asset Downtime?' box (This dictates operational impact).
4. Route Workflow and select Submit Work Order.

Scheduled Start:

Scheduled Finish:

☒ Requires Asset Downtime?

☒ Submit Work Order

OK

Step 2: Operations Approves the Downtime Schedule




Business Logic


Because PM work requires asset downtime, Operations must validate the schedule to ensure minimal disruption to the active business process. Rejections require the Service Engineer to revise.

Action Checklist (Operations)

- 1. Locate the PM Work Order in the Start Center Inbox / Assignments.
- 2. Select the Route Workflow icon.
- 3. Choose Approve Schedule.
- 4. Click OK.

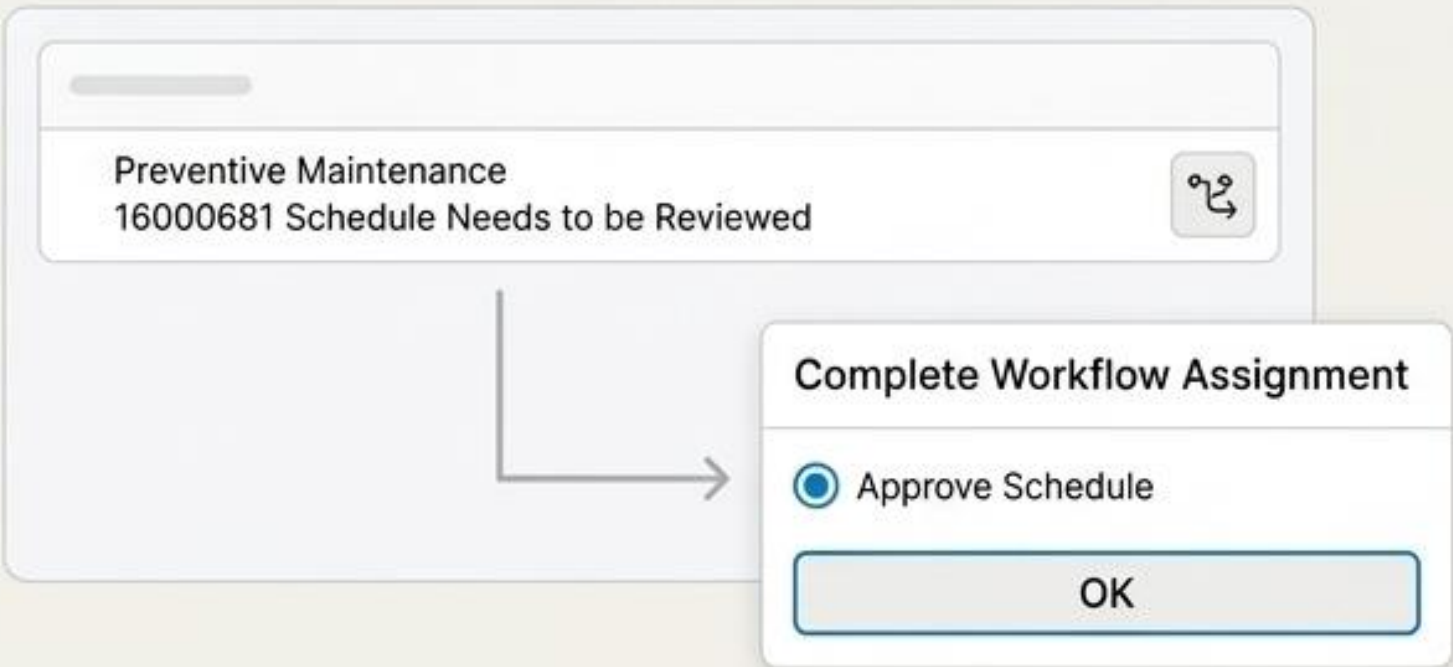


Step 3: Initiating Execution and Changing Status

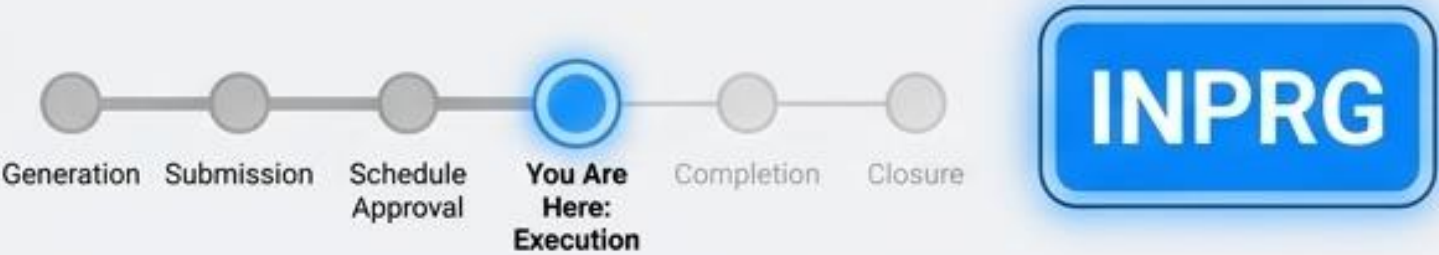

Action Checklist (Service Engineer)

- 1. Monitor **Start Center** for the newly approved assignment.
- 2. Route Workflow.
- 3. Select **Execute Work Order**.
- 4. System Status shifts to **INPRG** (In Progress).

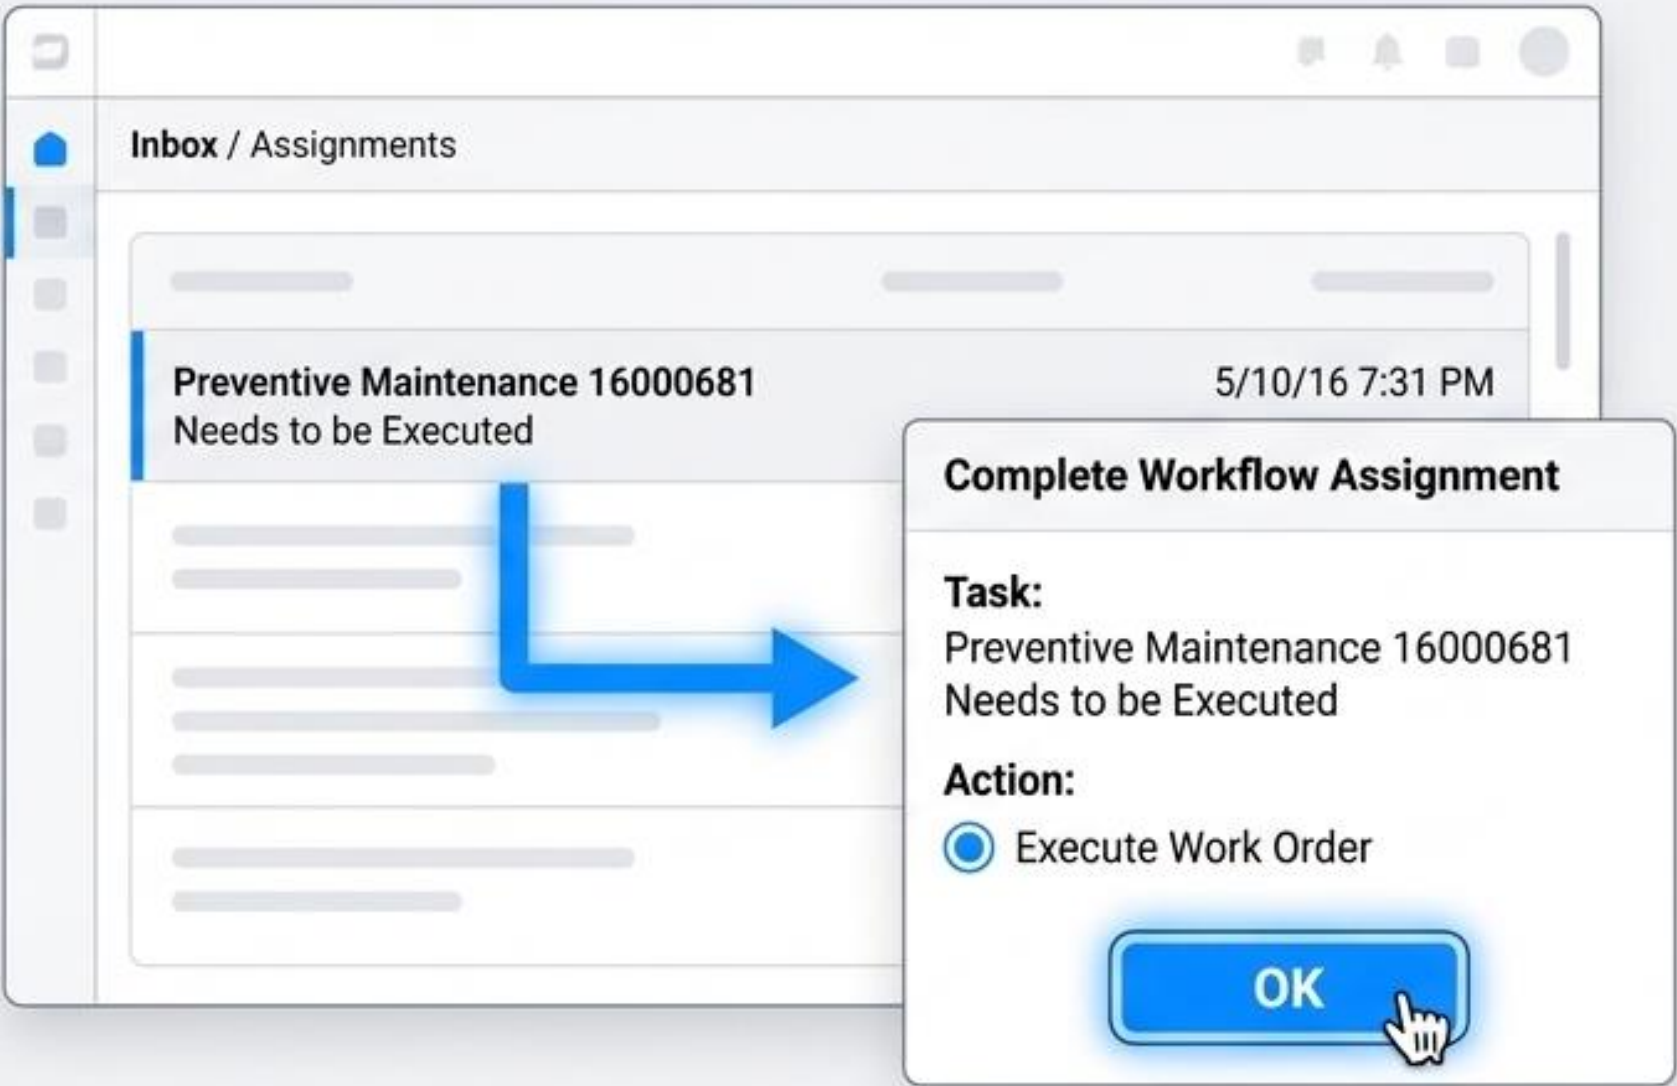

Step 4: Logging Results and Defining Downtime




Action Checklist (Service Engineer)

1. Navigate to Work Order Tracking via the main menu.
2. Search and select the specific Work Order number.
3. Route Workflow and select Complete Work Order.



MANDATORY: Define the Downtime Report

You must log the exact Start Date, End Date, and Total Hours before the system will allow completion.

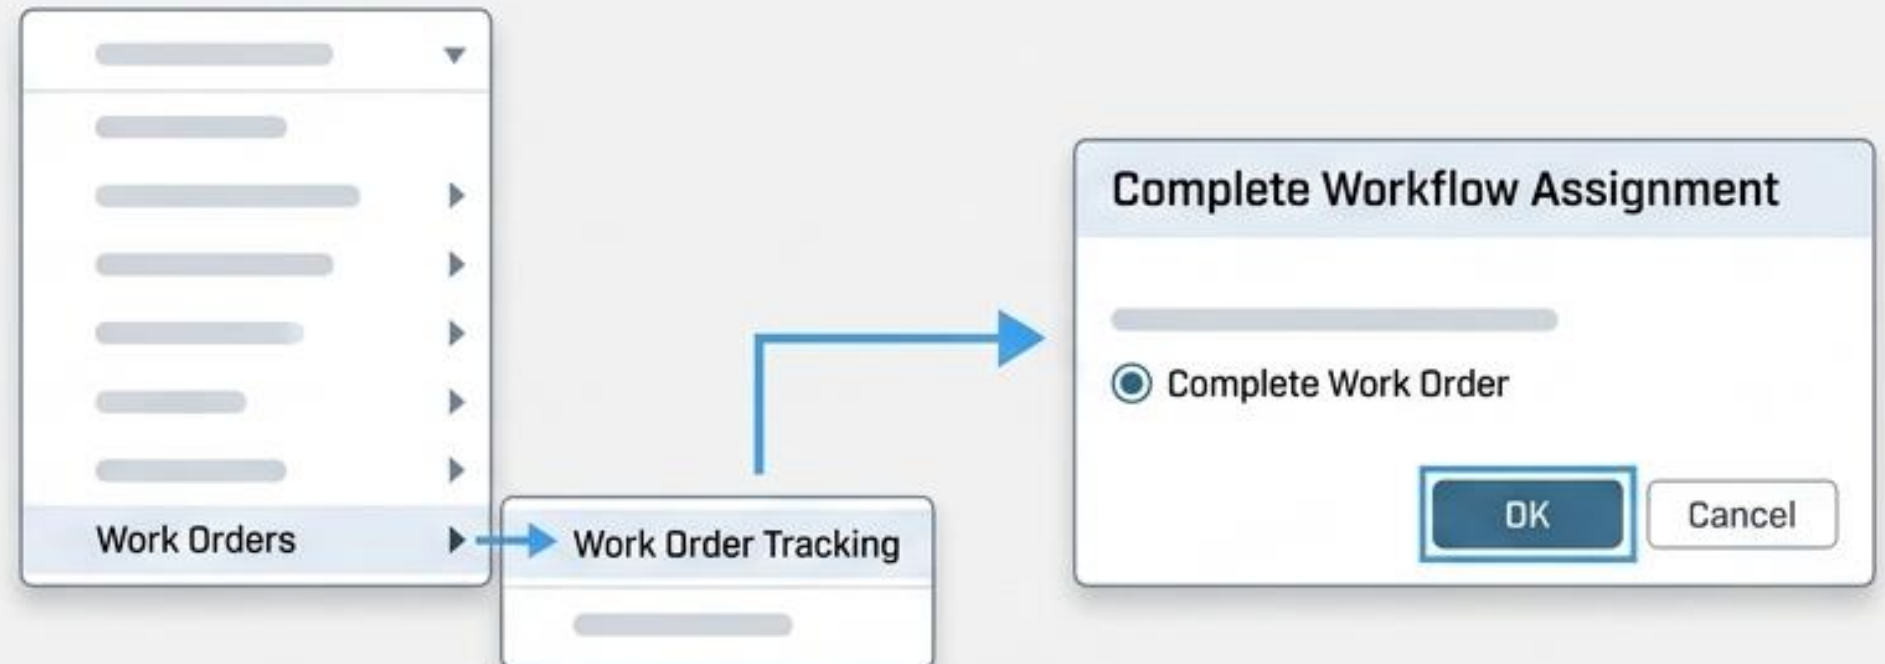


Step 5: Final Verification and Work Order Closure



Action Checklist (CHE Engineer)

1. Access the CHE Start Center Inbox.
2. Locate the Completed PM Work Order.
3. Route Workflow and select Close Work Order.

End State: The asset is returned to normal operation, and the ticket status is permanently updated to CLOSE.

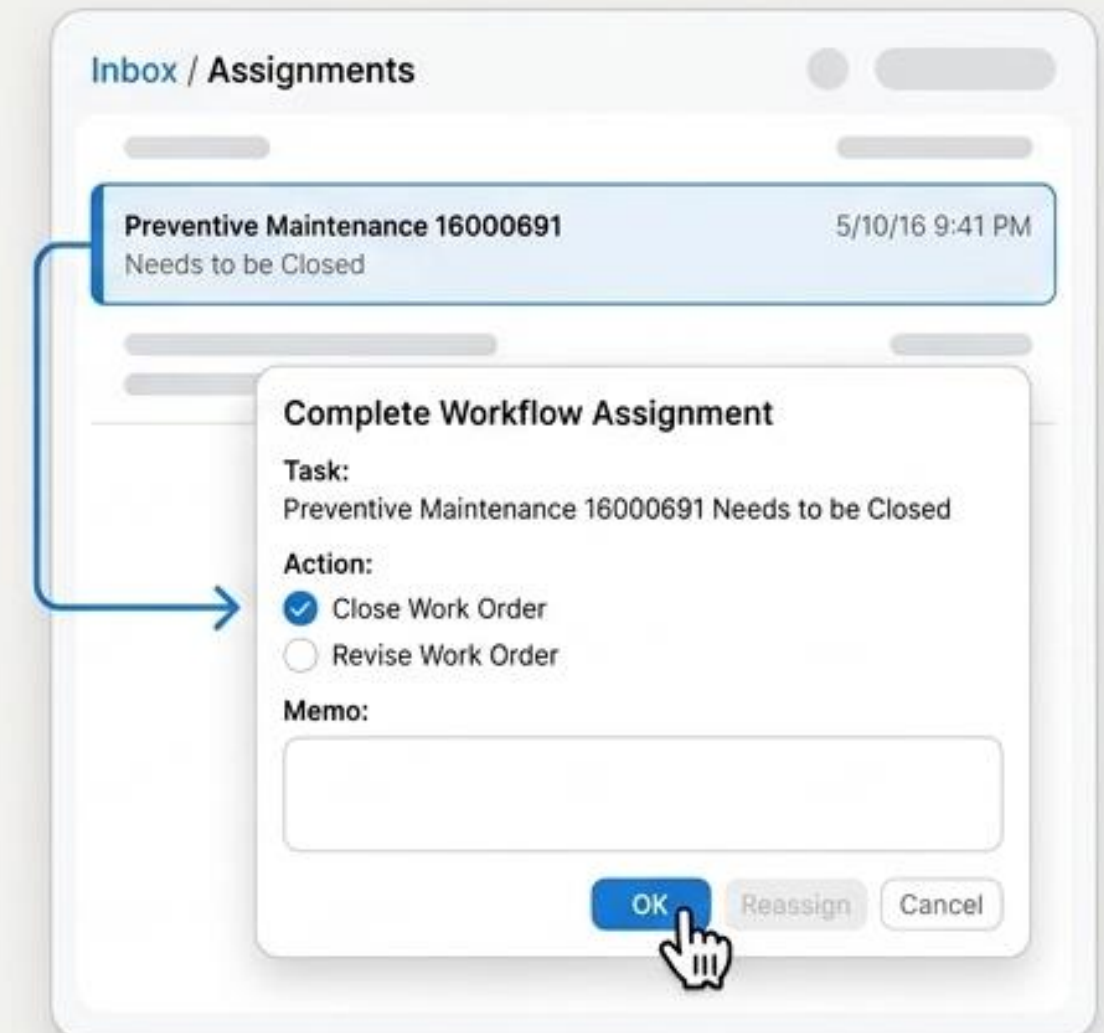


The Accelerated Lifecycle of a Daily Inspection (DI)



Key Insight


Unlike PMs, Daily Inspections rely on pre-registered Job Plan checklists and rarely require complex inter-departmental scheduling approvals.

Daily Inspections: The Execution vs. Cancellation Decision

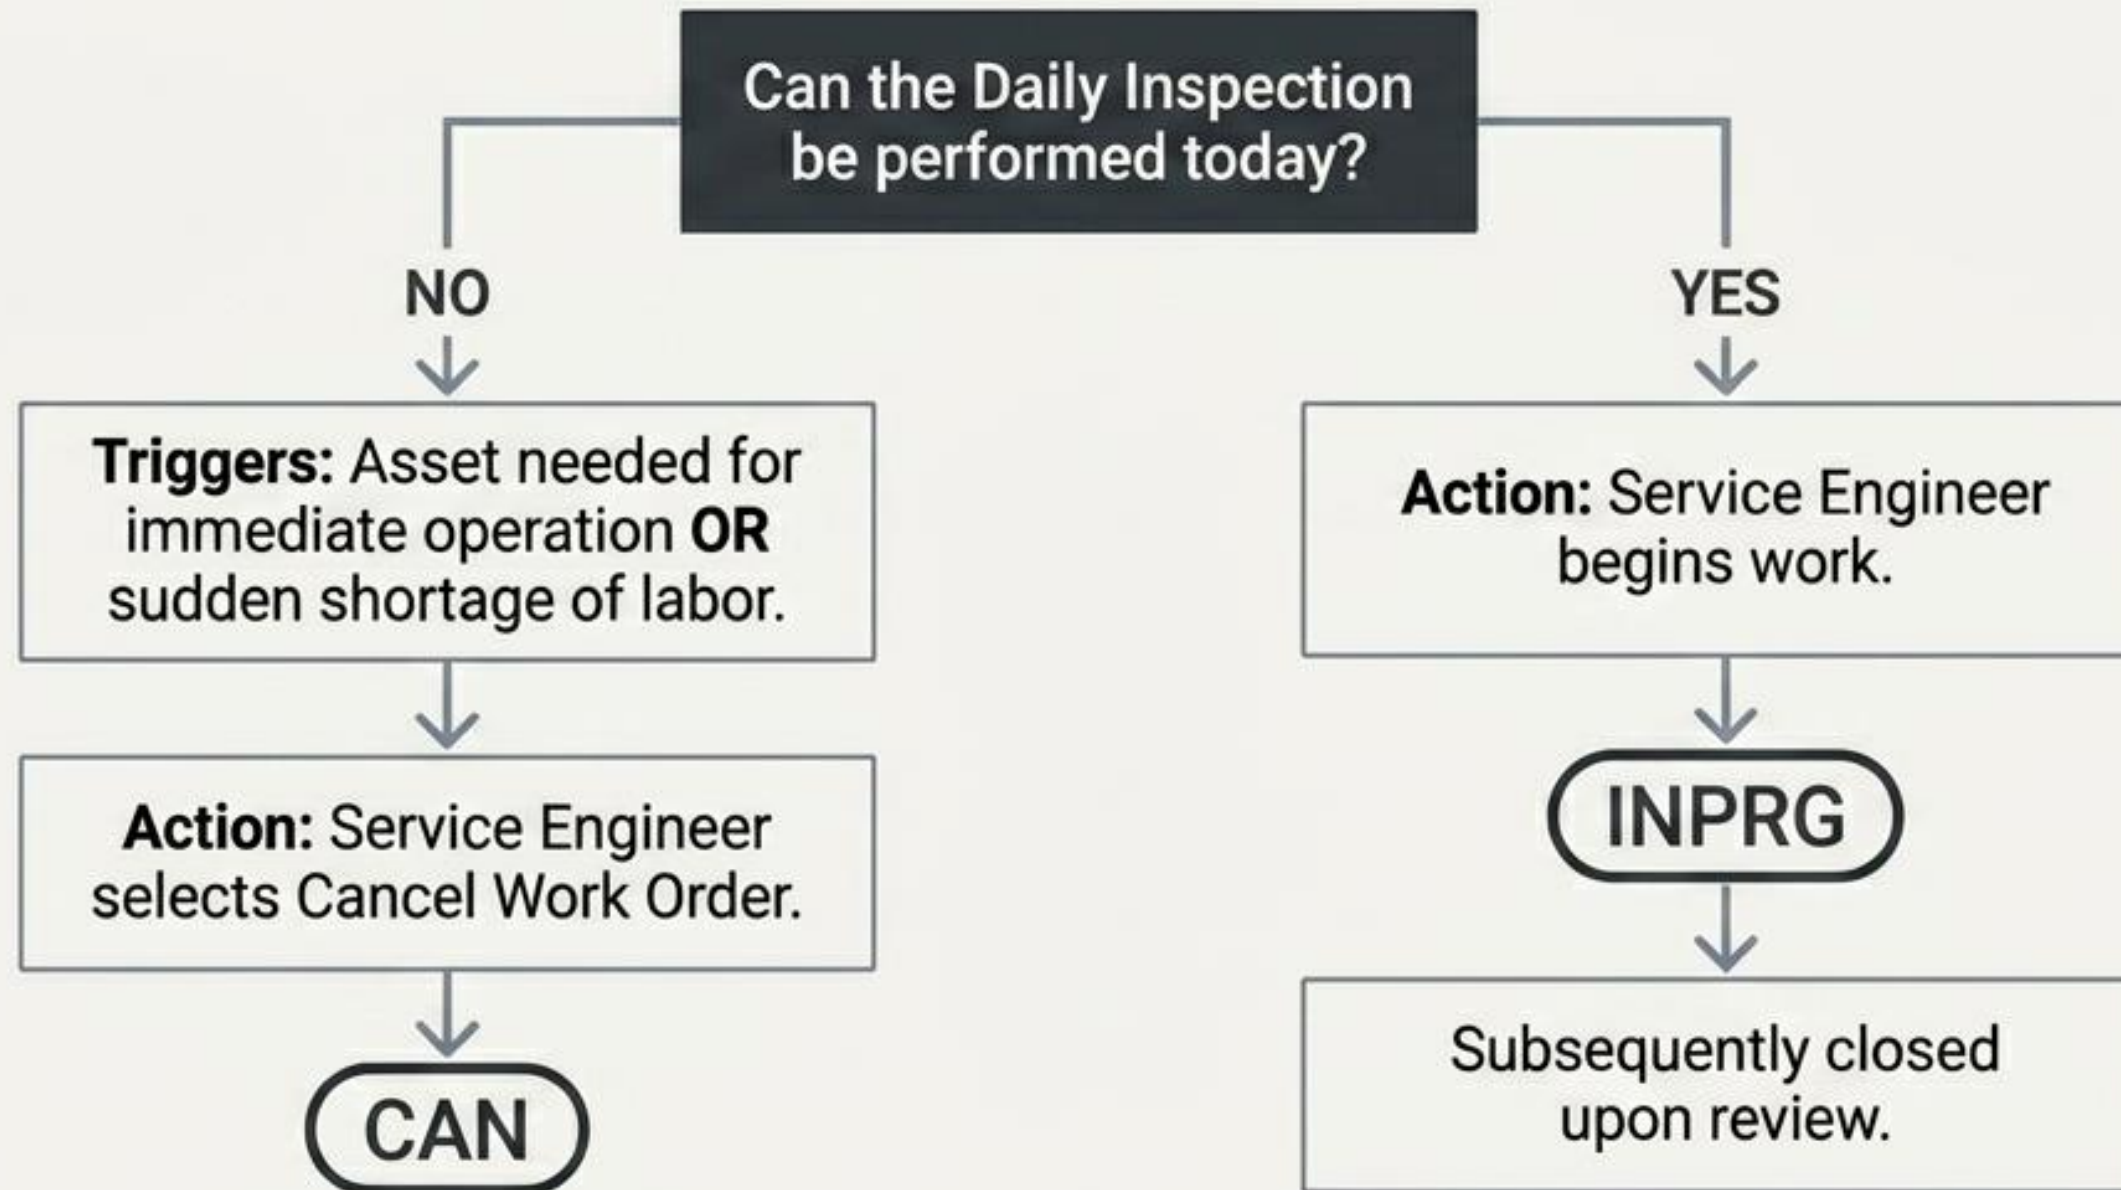

Escalation: Triggering Follow-Up Work from Inspections

Context: DIs are designed to detect incipient failures. When a checklist item fails, the Service Engineer must log the result and initiate follow-up maintenance.

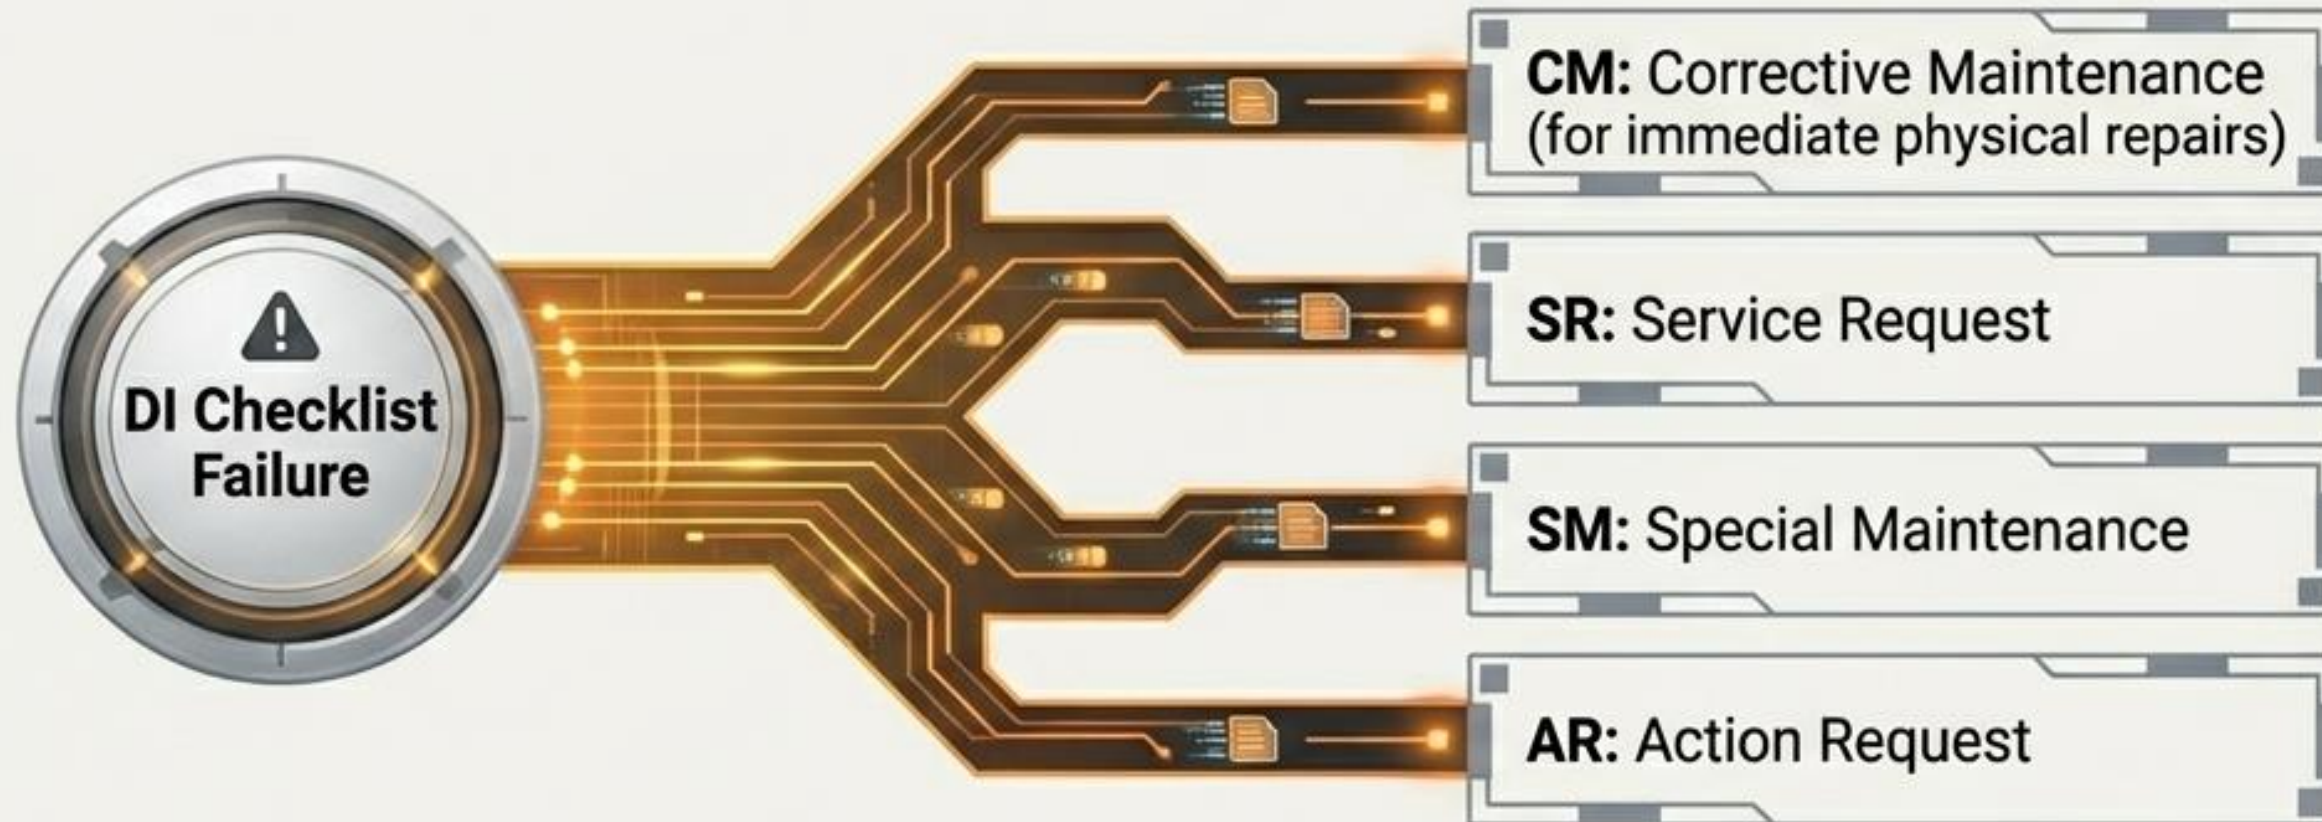

Takeaway: Daily Inspections are the early-warning sensors that populate the rest of the work management system.

System Status Glossary: The Language of the Control Room

APPR

(Approved)

Initial state of a newly generated PM Work Order.

WEXEC

(Waiting to Execute)

Initial state of a newly generated DI Work Order.

INPRG

(In Progress)

Work has been physically initiated by the Technician/Service Engineer.

COMP

(Completed)

Work is physically done, downtime is logged, waiting for final sign-off.

CLOSE

(Closed)

Final verification by the CHE Engineer. Record is permanently locked.

CAN

(Cancelled)

Work aborted due to operational needs or labor shortages (common in DIs).
